



KIIDC



PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

**UPGRADATION OF GOVT. ITI
KANNUR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount : Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion : 14-08-2021

Scheduled progress as on 24-07-2021 - 100 %

Achieved progress as on 24-07-2021 - 30 %

Last week progress - 30%

Current week progress - 30%

Current Bill Status :Under preparation

Current Financial Progress - 15 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 50% completed
- Steel works has to be started for pending columns, staircase, beams, slab etc
- Smart class room tile works finished.

Works done in the last week

- Smart classrooms selected and tile work finished.
- Pending backfilling of soil done.
- Currently labours at site and setting up site for the work



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM BRIDGE ACROSS KUPPAM
RIVER IN KOOVERY-KATTAMPALLY IN CHAPPARAPADAVU
PANCHAYAT , THALIPARAMBA TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Scheduled progress as on 24- 07-2021 - 100 %

Achieved progress as on 24- 07-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NA

Current Financial Progress - 0 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

Works done in the last week

- Topographical, GPS Survey works for land acquisition works has been done at both banks



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM
(KIIFB)**

**KIIFB PROJECT-
CONSTRUCTION OF
REGULATOR WITH LOCK
ACROSS ANCHARAKANDY
RIVER AT PARAPRAM IN
PINARAYI PANCHAYATH,
KANNUR DISTRICT**

Name of contractor : PGCC
Agreement date : 06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion :15-05-2022
Expected Date of completion :15-05-2022

Scheduled progress as on 24-07-2021 - 16%

Achieved progress as on 24-07-2021 - 8.85 %

Last week progress - 8.8%

Current week progress - 8.85%

Current Bill Status : First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 6.8%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Pier P2 (Left Bank) = 4th Lift (up to +3.70m) completed
- Abutment A1(Left Bank): 2nd lift completed (+0.30m)
- Wing Wall (Left Bank U/S): 1st Lift Completed (-0.6m)

Works done in the last week

- Abutment A1: 3rd lift concreting (+1.40m)
- Wing Wall (U/S): 2nd lift Concreting (+0.40m)
- Pier P2: 5th Lift concreting (+4.40m)
- Works delayed due to heavy rain



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

- 1. Andalurkavu**
- 2. Jagannath Temple**
- 3. Kottiyoor tourist Amenities**
- 4. Illikunnu church**
- 5. Lokanarkavu Temple**
- 6. Makreri Subramanyaswami Temple**

Andalurkavu

Name of contractor Vallamattam : Sri. Varkeychan T
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.518 Cr
Agreed Amount With GST : Rs. 1,70,11,777.6
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

Status:

- Agreement Executed.
- Work yet to be started

Jagannath Temple

Name of contractor : Sri. Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.481 Cr
Agreed Amount With GST : Rs. 1,65,96,091.2
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Electrification
- Trees and street furniture
- Revival of pond
- Compound wall

Status:

- Agreement Executed.
- Work yet to be started

Kottiyoor tourist Amenities

Name of contractor : Sri. Saji Varghese
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.749 Cr
Agreed Amount With GST : Rs. 1,95,91,008.6
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Dormitory and Clock room
- Ticket counter
- Tourist pilgrim shelter
- Electrical works
- Landscaping

Status:

- Agreement Executed.
- Work yet to be started

Illikunnu church

Name of contractor : Sri. Varkeychan T Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 0.798 Cr
Agreed Amount With GST : Rs. 89,38,493.08
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Landscaping of cemetery area
- Lighting
- Conservation of ceiling
- Woodwork
- Joinery
- Electrical works

Status:

- Agreement Executed.
- Work yet to be started

Lokanarkavu Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3.787 Cr
Agreed Amount With GST : Rs. 4,24,19,523.2
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Museum of Folklore
- Oottupura
- Thanthrimadam - Museum of Myth
- Conservation of Small Chira, Kulappura
- Compound wall and step
- Conservation of Big Chira
- Electrical works
- Plumbing and toilet fittings for differentially abled
- Pavement works & Landscaping

Status:

- Agreement Executed.
- Work yet to be started

Makreri Subramanyaswami Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 1.835 Cr
Agreed Amount With GST : Rs. 2,05,52,642.3
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Oottupura
- Toilet Block
- Landscaping
- Electrical
- Streetscape (Paving of Chuttambalam)
- Water supply and Sanitary Arrangements
- Stone Paving
- Conservation of pond
- Electrification

Status:

- Agreement Executed.
- Work yet to be started
- MoU to be signed.

PROJECTS IN WAYANAD DISTRICT

**KARAPUZHA PHASE
III
(TOURISM)**

**KARAPUZHA PHASE III
CONSTRUCTION OF VIEWING
TOWER, BAMBOO PAVILION
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P
Agreement date : 22/12/2017
Agreed Amount : ₹ 7248330.00
Agreed Amount With GST : Rs. 725000.00
Site Handover date : 29/12/2017
Project duration : 10 months
Scheduled Date of Completion :29/10/2018
Expected Date of completion :15/07/2021

Status of Work in terms of components:

- Viewing tower-96.5%
- Bamboo pavilion-100%
- Bridge.-100%

Works done in the last week

- Work delayed due ti rain

Scheduled progress as on 24-07-2021 100%

Achieved progress as on 24-07-2021 - 0 %

Last week progress in 0%

Current week progress - 0%

Current Bill Status :3rd bills submitted of amount 41,40,724.00

Current Financial Progress :60%

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion : 13-08-2021
Expected Date of completion : 13-09-2021

Status of Work in terms of components:

- Main Building Civil works – 75%
- Main Building Electrical works – 75%
- Main Building ELV Works - 60%

Works done in the last week

- Main Building Civil works
- Main Building Electrical works
- Main Building Plumbing works

Scheduled progress as on 23-07-2021 - 95%

Achieved progress as on 23-07-2021 - 50%

Last week progress in 44%

Current week progress in 50%

Current Bill Status : CC 1st and part submitted for an amount of Rs 52,57,968.6/-

Current Financial Progress : 25.8%

Images of works done at Site during last week (with time stamp)



**PERUVANNAMOO
ZHI (TOURISM)**

**DEVELOPMENT OF
PERUVANNAMOOZHI DAM
TOURISM PROJECT IN
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N
Agreement date : 06-11-2020
Agreed Amount : ₹ 26359270.97
Agreed Amount With GST : Rs. 31388620.00
Site Handover date : 13/11/2020
Project duration : 9 months
Scheduled Date of Completion : 12-08-2021
Expected Date of completion : 30-09-2021

Status of Work in terms of components:

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate

Works done in the last week

- Childrens park-fencing works
- Construction of new gate-earthwork excavation for column footing.
- Electrification works.

Scheduled progress as on 24-07-2021 - 50%

Achieved progress as on 24-07-2021 - 48 %

Last week progress in 30%

Current week progress in 35 %

Current Bill Status : 1st bill-46,10,745.21

Current Financial Progress :20%

Images of works done at Site during last week (with time stamp)



**RCB
PERINCHERIKADA
VU
(KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE AT
U/S OF PERINCHERIKADAVU IN
KUTTIADY RIVER
(GULIKAPUZHA) AT
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 6,11,33,413.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022
Expected Date of completion :16-09-2022

Status of Work in terms of components:

- RCB – 2% (two piles casted)
- Bank Protection works – 1%
- Material collection works are going on.(Coconut posts supplying)

Works done in the last week

- The cross bund constructed was dismantled as per the instruction from Higher authorities of Irrigation department and local bodies. No works are possible in river without the bund.
-

Scheduled progress as on 23-07-2021 - 51%

Achieved progress as on 23-07-2021 - 2%

Last week progress in 2%

Current week progress 2%

Current Bill Status : NIL

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

**KIIFB Project - Construction of
Regulator at Puzhankavu across
Kadalundi River**

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021
Expected Date of completion :15/02/2022

Status of Work in terms of components:

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

Works done in the last week

- Work is delayed due rainfall and rise in water level.

Scheduled progress as on 24-07-2021- 100 %

Achieved progress as on 24-07-2021 - 55%

Last week progress in 55 %

Current week progress in 55 %

Current Bill Status : Total Bill submitted ₹3 Crores

Current Financial Progress in %: 8.67%

Images of works done at Site during last week



**RCB
Moothikkayam
(KIIFB)**

**KIIFB Project construction of
regulator cum bridge across
thoothapuzha keezhmurikadavu
moothikkayam in moorkanad
panchayath**

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022
Expected Date of completion :26/12/2022

Status of Work in terms of components:

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

Works done in the last week

- No work has done due to monsoon.
- Consolidated survey nos for LA
-

Scheduled progress as on 23/07/2021 - 58 %

Achieved progress as on 23/07/2021 - 3%

Last week progress - 3%

Current week progress - 3%

Current Bill Status : First & part bill submitted – Rs 1.03 Cr

Current Financial Progress : 1.75%

Images of works done at Site during last week (with time stamp)



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMBUZHA
(KASE)**

**UPGRADATION OF GOVT. ITI
MALAMPUZHA ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS
Agreement date : 05/03/20
Agreed Amount : ₹11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date : 16/03/2020
Project duration : 18 months
Scheduled Date of Completion : 05/09/2021
Expected Date of completion : 29/06/22

Status of Work in terms of components:

- Main building part 2 roof slab completed
- Initial pile load test,routine test
- Smart classroom flooring and painting completed.
- Lower basement plinth beam steel work and retaining wall steel work under progress
- FF part 1 area column rising completed.

Works done in the last week

- Pile cap casting 100%
- Lift area soil backfilling 95%
- Pile cap soil backfilling 100%
- UGF block work under progress
- LGF plinth beam and retaining wall steel work under progress
- LGF roof slab concreted.
- UGF plinth beam pcc work.

Scheduled progress as on 23/07/2021- 92%

Achieved progress as on 23/07/2021 - 32%

Last week progress - 1%

Current week progress - 2%

Current Bill Status : no of bill submitted - 1, amount:- 68,83,336

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Scheduled progress as on 24/07/2021 - 38 %

Achieved progress as on 24/07/2021 - 27 %

Last week progress - 1%

Current week progress - 1%

Current Bill Status : 1 st bill submitted of 1.56 cr

Current Financial Progress : 0%

Images of works done at Site during last week

Status of Work in terms of components:

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(35m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 2 pier and 2nd Lift of 3 pier is completed

Works done in the last week

- No major civil works due to high flood



**Moongilmada LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹33288750 Crores
Agreed Amount With GST : Rs. 37283400/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Sub-main Line Works

Scheduled progress as on 24/07/2021 - 40 %

Achieved progress as on 24/07/2021 - 40.5 %

Last week progress in : 40%

Current week progress : 0.5%

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



**Karadippara LIS
(WRD-RKI)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district**

Name of contractor :M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹2,34,53,555.40 Crores
Agreed Amount With GST : Rs. 26267982.04/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Main Line work

Scheduled progress as on 24/07/2021 - 42 %

Achieved progress as on 24/07/2021 - 84 %

Last week progress in : 84 %

Current week progress in 0%

Current Bill Status : NO

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**Karadipara
(Civil)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district-Civil**

Name of contractor :M/s Vallamattam constructions
Agreement date : 26-02-2021
Agreed Amount : ₹16,41,529.18 Lakhs
Agreed Amount With GST : Rs. 18,38,512.68/-
Site Handover date : 26-02-2021
Project duration : 6 months
Scheduled Date of Completion :26-08-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Construction of Pump House
- Electrification

Works done in the last week

- Roof slab Concrete
-Curing period

Scheduled progress as on 24/07/2021 - 30 %

Achieved progress as on 24/07/2021 - 52 %

Last week progress in : 52%

Current week progress in 0%

Current Bill Status : No

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN THRISSUR DISTRICT

ITI CHALAKUDY

**UP GRADATION OF GOVT ITI
CHALAKUDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

Scheduled progress as on 24-07-2021 - 0 %

Achieved progress as on 24-07-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)


Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the

last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

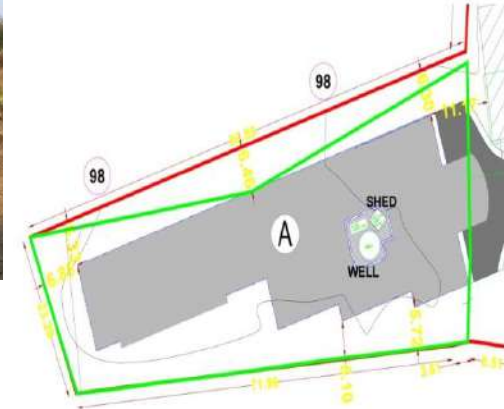

PROJECTS IN ERNAKULAM DISTRICT

**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion :

Status of Work in terms of components:

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

Works done in the last week

- NO WORK

Scheduled progress as on 24-07-2021 - 21 %

Achieved progress as on 24-07-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO
DU CANAL
(KIIFB)**

**IMPROVEMENTS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY**

Name of contractor : Southern Tech
Agreement date : 08-10-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration :15 months
Scheduled Date of Completion :07-01-2020
Expected Date of completion :30-08-2021

Status of Work in terms of components:

- Cleaning & desilting- completed
- Side protection work- 81%
- Road and walkway formation- 58%
- Fencing and Handrail work-53%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%(tile work remaining)

Works done in the last week

- Fixing GI post ch320-900 (RB)
- Epoxy painting - fencing post ch320-690 (RB & LB)
- Welding & placing the fencing frame Ch 0-900(RB)

Scheduled progress as on 24-07-2021 - 98%

Achieved progress as on 24-07-2021 - 93%

Last week progress - 92.5%

Current week progress -93%

Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING
STREET LIGHTS ALONG THE
PATHWAYS OF
ANTHAKARATHODE**

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 08-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 31-07-2021

Status of Work in terms of components:

- Excavation and supply Laying of cable-50%
- Placing of lamp post, LED & feeder -30%
- Excavation and concreting-65%

Works done in the last week

- No work

Scheduled progress as on 24-07-2021- 85%

Achieved progress as on 24-07-2021- 44%

Last week progress - 43%

Current week progress 44%

Current Bill Status : First and Part Bill prepared

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

**UP GRADATION OF GOVT ITI
KATTAPPANA ON PAR WITH
INTERNATIONAL
STANDARDS**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 24-02-2022
Expected Date of completion : 24-02-2022

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 7 %
- Grade beam concrete- 2%

Works done in the last week

- . Grade beam reinforcement work.
- Grade beam concrete

Scheduled progress as on 24-07-2021 - 22%

Achieved progress as on 24-07-2021 - 19.5%

Last week progress : 19.2%

Current week progress :19.5%

Current Bill Status : NIL

Current Financial Progress in %:NIL

Images of works done at Site during last week



**PAVANATHA
COLLAGE
MURIKKASSERY
(RUSA)**

**RUSA II PROJECT -
CONSTRUCTION-PAVANATHMA
COLLEGE MURIKKASSERI,
IDUKKI.**

Name of contractor : Anchanical constructions
Agreement date : 02.12.2019
Agreed Amount : Rs.79,00,000
Agreed Amount With GST : Rs.93,22,000
Site Handover date : 02-06-2020
Project duration : 09 months
Scheduled Date of Completion :31-08-2021
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

Works done in the last week

- No works done.

Scheduled progress as on 24-07-2021 - 86%

Achieved progress as on 24-07-2021 - 89%

Last week progress : 89%

Current week progress in : 89%

Current Bill Status : 2 Bills submitted, RS 54,77,389.30

Current Financial Progress : 69%

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – I
(TOURISM)**

**ADDITIONAL WORK I OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
APPROACH ROAD,RETAINING
WALL,DRAIN AND STREET
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 11-08-2020
Agreed Amount : Rs.69,50,003.24
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 21-08-2020
Project duration : 04 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 08-07-2021

Status of Work in terms of components:

- Interlocking pathway 90%
- Gate installation 30%
- Providing street lights - 50%

Works done in the last week

- Pathway interlocking
- Rain delayed work progress.

Scheduled progress as on 24-07-2021 - 91%

Achieved progress as on 24-07-2021 - 95%

Last week progress : 94%

Current week progress : 95%

Current Bill Status : 1 Bill submitted, RS 36,27,077.98.

Current Financial Progress : 52%

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 13-09-2021

Scheduled progress as on 25-07-2021 - 63 %

Achieved progress as on 25-07-2021 - 27 %

Last week progress in % -26.4%

Current week progress - 27%

Current Bill Status : under preparation

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Roofing works of guest house building is completed
- 95% of roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building completed.

Works done in the last week

- Roofing works of guest house building



PANCHALIMEDU
(TOURISM)

PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAMVILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2021

Scheduled progress as on 25-07-2021 - 33 %

Achieved progress as on 25-07-2021 - 17 %

Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

Works done in the last week

- Steel reinforcement works for check dam
- Work stopped due to heavy rain and mist.



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

**UP GRADATION OF GOVT ITI
ETTUMANOOR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : Within this Financial Year

Scheduled progress as on 24/07/2021- 88 %

Achieved progress as on 24/07/2021 - 43 %

Last week progress - 43%

Current week progress - 1%

Current Bill Status : CC 3rd and part is submitted (total : ₹ 2,24,79,461.06)

Current Financial Progress : 32%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (70%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting (0%)
- Fire protection works (0%)
- Furniture for existing smart class room
Converted to smart class rooms (0%)

Works done in the last week - Main building civil works

- AAC block work on FF
- Lintel and sunshade shuttering and reinforcement works on UGF.
- Electrical concealed works
- Fin wall at front UGF
- Porch PCC, Plastering



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE
INSTITUTE OF HOTEL
MANAGEMENT STUDIES AT
PALA, KOTTAYAM DISTRICT,
CONSTRUCTION OF ACADEMIC
BLOCK**

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Scheduled progress as on 24/07/2021 - 88%

Achieved progress as on 24/07/2021 - 79%

Last week progress -79%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 74 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works done in the last week

- Water tank cover slab shuttering and reinforcement works



**CHEEPUNKAL
(TOURISM)**

**KIIDC KUMARAKOM
CHEEPUNKAL DESTINATION
DEVELOPMENT PROJECT AT
AYMANAM PANCHAYAT IN
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1,19,66,517.41
Agreed Amount With GST : ₹ 1,34,02,499.49
Site Handover date : 05-05-2021
Project duration : 12 months
Scheduled Date of Completion : 04-05-2022
Expected Date of Completion : 04-05-2022

Status of Work in terms of components:

- House Boat Jetty (0%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

Works done in the last week - Main building civil works

- Reinforcement work for Pile

Scheduled progress as on 24/07/2021-

Achieved progress as on 24/07/2021 - Nil

Last week progress -

Current week progress -

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR
WITH INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date :23/10/2020
Project duration :18 months
Scheduled Date of Completion : 22/04/2022
Expected Date of completion :22/3/2022

Scheduled progress as on 24/7/2021 -39%

Achieved progress as on 24/07/2021 -Nil

Last week progress in - Nil

Current week progress in - Nil

Current Bill Status : (no: of bills submitted with amount) Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)- Nil

Status of Work in terms of components:

- Main building civil works (0%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room

Works done in the last week

- Tree cutting has been taken for open tender, and the amount accepted has given to directorate for approval.The accepted amount has been given to government for approval.
- Meeting was arranged on 15/7/2021 by KASE,KIIDC AND CHENGANNUR ITI Principal and discussed the various issue regarding the treecutting and KIIFB query and sorted out conclusion

**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

**MODERNIZING WATER
TRANSPORT IN ALAPPUZHA
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-09-2021

Status of Work in terms of components:

- Cleaning of Canals Completed
- Deepening of Canals after dewatering Completed
- RR Masonry side protection
 - Main Canals Completed
 - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
 - Culvert Structural Works Completed
 - Approach wall Under progress

Works done in the last week

- Bund removal for Bernad, Devi wire and Ambanakulangara culverts
- DR work for subcanals.
- Guard stone work for Devi wire and Aryad block culvert

Scheduled progress as on 24/07/2021 - 100%

Achieved progress as on 24/07/2021 - 92.00%

Last week progress in 91.75%

Current week progress- 0.25%

Current Bill Status : Rs.38,13,65,683.22 upto 4th bill

Current Financial Progress : 70%

Images of works done at Site during last week (with time stamp)



**PUNNAMADA
(TOURISM WORK)**

**Punnamada- Starting Point
Pathway and Boat Landing at
Alapuzha District.**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 04-11-2021
Expected Date of completion : 04-11-2021

Status of Work in terms of components:

- Pathway
Solar Lighting

Works done in the last week

- The mobilization works for carrying out the components under progress

Scheduled progress as on 24/07/2021- 20%

Achieved progress as on 24/07/2021 - 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL
)- KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 04-02-2022

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- The mobilization works for carrying out the components under progress

Scheduled progress as on 24/07/2021 - 15%

Achieved progress as on 24/07/2021 - 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

- 20m groynes – (5 nos) - Not Started
- 30M GROYNES - 7nos- 2 completed
- 40M GROYNES – 9 nos - 1 in progress
- 50M GROYNES – 9 nos - 3 in progress
- Sea wall length - 305 m – Not started
- 30514 MT boulders reached out of 178922 MT (17%)
- 2T TETRAPODS – 6843 nos. casted out of 23902 nos.
- 5T TETRAPODS – 547 nos. casted out of 2956 nos.
- Earthwork Excavation – 9359.27m3 completed out of 45955.7 M3

Works done in the last week

- 2T tetrapod casted - 254 nos.
- 5T tetrapod casted -7 nos.
- Supplying and Laying of Boulders - 5768.73 MT
- laying of boulders for G5, G6 and G8 are in progress.
- Groyne work started for G7
- Earthwork Excavation and geomat laying was done for G7

Scheduled progress as on 24-07-2021 – 60 %

progress as on 24-07-2021 - 25.9%

Last week progress - 3 %

Current week progress - 3 %

Current Bill Status : 2 bill submitted for an Amount of Rs. 11,23,21,298

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

- 1.20M GROYNES - 6 NOS-Not started
- 2. 25M GROYNES - 15 NOS-Not started
- 3. SEA WALL LENGTH - 40m
-Not started
- 4. TOTAL QUANTITY OF BOULDERS - 94497 MT
- 7. 2T TETRAPODS -704 nos casted out of 9874 NOS
- 8. 5T TETRAPODS - 2385 NOS
- 9. GEOMAT - 64739 M2
- 10. EARTHWORK EXCAVATION - 3290 M3

Works done in the last week

-Tetrapod casting is started and Total no of cased tetrapods, 2T-175nos

Scheduled progress as on 24/07/2021 - 60%

Achieved progress as on 24/07/2021 - 2%

Last week progress -1.5%

Current week progress -1.5%

Current Bill Status :1 part bill susubmitted for an amount of Rs 1715000.00

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of contractor : Ramalingam construction Company Pvt. Lmtd.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

1. 20M GROYNES - 2 NOS-One is started and in progress
2. 30MGROYNES -4 NOS-One is started and is in progress
3. 50M GROYNES - 7 NOS- Not started
- 4.3149.12MT boulders reached out of 74546 MT
5. 2T TETRAPODS -3515casted out of 8930NOS
6. 5T TETRAPODS -175 nos casted out of 1199NOS
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154 M3

Works done in the last week

- 2T and 5T tetrapod casting is in progress
- The total no.of tetrapods casted 2T-95 and 5T-16nos
- Geomat layed for G2
- Supplying and laying of boulders-2730.MT

Scheduled progress as on24/07/2021 - 60%

Achieved progress as on 24/07/2021 -13%

Last week progress in - 3.5%

Current week progress in 3.5%

Current Bill Status : 2 part bills submitted for an amt of Rs 23596744.04

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

1. 20M GROYNES - 2NOS-Not started
2. 30M GROYNES -10 NOS-Not started
3. 40M GROYNES - 4 NOS- Not started
4. TOTAL QUANTITY OF BOULDERS - 101487 MT
5. 2T TETRAPODS - 2718nos casted out of 8941 NOS
6. 5T TETRAPODS - 3432 NOS
7. GEOMAT - 76299M2
8. EARTHWORK EXCAVATION – 6239M3

Works done in the last week

-The total no.of tetrapods casted
2T -192nos and
5T is 0

Scheduled progress as on 24/07/2021 - 60 %

Achieved progress as on 24/07/2021 - 6.5 %

Last week progress 2%

Current week progress -2%

Current Status : 2 part bills submitted for an amt of Rs15862000.00

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**GROYNES SITE AT
KATTOOR
(KIIFB)**

Construction of 34 nos. Groyne at Kattoor
from Ch.168.465KM TO CH 171.627KM (Old CH 96.643KM TO CH
9.535 KM)

Name of contractor : Ramalingam Construction
Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Scheduled progress as on 24-07-2021 – 60 %

Achieved progress as on 24-07-2021 - 19.30 %

Last week progress - 3.5 %

Current week progress - 4 %

Current Bill Status : 2 bill submitted for an Amount of Rs. 7,01,81,077.49

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groynes - 3 nos – Not started
- 30m Groynes -7 nos – not started
- 40m groynes - 24 nos- not started
- Laying of boulders - Not started
- 2T TETRAPODS – 7749 nos.
casted out of 21562 nos.
- 5T TETRAPODS – 405 nos. casted
out of 3144 nos.
- Geomat - 112083 m2
- Earthwork Excavation - 42122 M3

Works done in the last week

- 2T tetrapod casted -352 nos.
- 5T tetrapod casted - 42 nos.
- Supplying and Laying of Boulders - 7700 MT
- laying of boulders for G13 are in progress.
- Groyne work started for G14
- Earth work and mat laying also done for G13 and G 14



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion : 23-08-2021
Expected Date of completion : 31-12-2021

Scheduled progress as on 23/07/2021 - 75 %

Achieved progress as on 23/07/2021 - 13%

Last week progress -10.5%

Current week progress -13%

Current Bill Status : (no: of bills submitted with amount) - NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works –18%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 18%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- Main building civil works - Grade beam concreting done, deshuttering completed
-



**Thenmala
(Tourism Project)**

**IMPROVEMENT AND
DEVELOPING ECO-TOURISM AT
THENMALA DAM IN KOLLAM
DISTRICT**

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹4.5 Cr
Agreed Amount With GST : Rs. 4,49,90,000.00
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 07-01-2022

Status of Work in terms of components:

- SHOP (7.1%)
- Shed to shop (40%)
- Building Renovation (35%)
- Children play (1%)
- Water tank (10%)

Works done in the last week

- Shop- lintel completed in two span.
- Brick work started
- Clearing children play area
- Excavation of water tank
- Pcc for water tank
- Reinforcement work for water tank started
- Water tank column for

Scheduled progress as on 24/07/2021 - 45%

Achieved progress as on 24/07/2021 - 8%

Last week progress in -8%

Current week progress -2%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)



**ITI
DHANUVECHAPU
RAM
(KASE)**

**UPGRADATION OF GOVT. ITI
DHANUVECHAPURAM ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion : 03-08-2021
Expected Date of completion : 03-08-2021

Scheduled progress as on 23-07-2021- 78%

Achieved progress as on 23-07-2021 - 68.80%

Last week progress - 65%

Current week progress - 69%

Current Bill Status :6 bill were passed, Amount up to 8th bill:55712783.40/-
,8th bill submitted amount:3784498.15/-

Current Financial Progress :49%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 90% completed
- GF primer work 80% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 30% completed
- FF Block Work 92% completed
- FF Ceiling work 70% completed
- FF plastering 85% completed
- Dummy column RCC completed
- FF Electrical concealed work 65% completed
- Parapet plastering 90% completed
- GF Tile work 52%
- FF primer work 60% completed

Works done in the

last week

- Outside Plastering
- Reinforcement work for the construction of car porch
- GF-Toilet Wall Tiling work

