



KIIDC



# **PROJECTS IN KANNUR DISTRICT**

**ITI KANNUR  
(KASE )**

**UPGRADATION OF GOVT. ITI  
KANNUR ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount : Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion : 14-08-2021

Scheduled progress as on 30-07-2021 - 100 %

Achieved progress as on 30-07-2021 - 30 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : 1st bill submitted

Current Financial Progress - 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 60% completed
- Steel works has to be started for pending columns, staircase, beams, slab etc
- Smart class room tile works finished.

**Works done in the last week**

- Column Reinforcement and concreting were done.



**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY  
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM BRIDGE ACROSS KUPPAM  
RIVER IN KOOVERY-KATTAMPALLY IN CHAPPARAPADAVU  
PANCHAYAT , THALIPARAMBA TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd  
Agreement date : 15-10-2019  
Agreed Amount : ₹ 18,57,64,823.98  
Agreed Amount With GST : 22,03,74,512.96 (as per RE)  
Site Handover date : 07-11-2019  
Project duration : 18 months  
Scheduled Date of Completion : 07-05-2021  
Expected Date of completion : NA

**Status of Work in terms of components:**

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

**Works done in the last week**

- Topographical, GPS Survey works for land acquisition works has been done at both banks

**Scheduled progress as on 30- 07-2021 - 100 %**

**Achieved progress as on 30- 07-2021 - 0 %**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NA**

**Current Financial Progress - 0 %**

**Images of works done at Site during last week (with time stamp)**



**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM  
(KIIFB)**

**KIIFB PROJECT-  
CONSTRUCTION OF  
REGULATOR WITH LOCK  
ACROSS ANCHARAKANDY  
RIVER AT PARAPRAM IN  
PINARAYI PANCHAYATH,  
KANNUR DISTRICT**

Name of contractor : PGCC  
Agreement date : 06-11-2020  
Agreed Amount : ₹44.49 Cr  
Agreed Amount With GST : Rs. 498,385,551.00  
Site Handover date : 16-11-2020  
Project duration : 18 months  
Scheduled Date of Completion : 15-05-2022  
Expected Date of completion : 15-05-2022

Scheduled progress as on 31-07-2021 - 17%

Achieved progress as on 24-07-2021 - 9 %

Last week progress - 8.85%

Current week progress - 9%

Current Bill Status : First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 7%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Wing Wall (Left Bank D/S Retaining wall upto Apron portion): Completed
- Wing Wall (Left Bank U/S Retaining wall upto Apron portion): Completed

**Works done in the last week**

- Abutment A1: 5th lift concreting (+3.50m)
- Wing Wall (U/S): Final lift concreting (+2.50m)
- Pier P1: 6th Lift concreting (+4.70m)
- Pier P2: 7th Lift concreting (+5.70m)
- Bank Protection Works (U/S Left Bank): Excavation completed. Foundation PCC completed





**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

- 1. Andalurkavu**
- 2. Jagannath Temple**
- 3. Kottiyoor tourist Amenities**
- 4. Illikunnu church**
- 5. Lokanarkavu Temple**
- 6. Makreri Subramanyaswami Temple**

## Andalurkavu

**Name of contractor** Vallamattam : Sri. Varkeychan T  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.518 Cr  
**Agreed Amount With GST** : Rs. 1,70,11,777.6  
**Site Handover date** : 08-03-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

### Approved components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

### Status:

- Agreement Executed.
- Work yet to be started

## Jagannath Temple

**Name of contractor** : Sri. Joseph R V  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.481 Cr  
**Agreed Amount With GST** : Rs. 1,65,96,091.2  
**Site Handover date** : 08-03-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

### Approved components:

- Pathway
- Electrification
- Trees and street furniture
- Revival of pond
- Compound wall

### Status:

- Agreement Executed.
- Work yet to be started

### Kottiyoor tourist Amenities

**Name of contractor** : Sri. Saji Varghese  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.749 Cr  
**Agreed Amount With GST** : Rs. 1,95,91,008.6  
**Site Handover date** : 08.03.2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

#### Status of Work in terms of components:

- Dormitory and Clock room
- Ticket counter
- Tourist pilgrim shelter
- Electrical works
- Landscaping

#### Status:

- Agreement Executed.
- Work yet to be started

### Illikunnu church

**Name of contractor** : Sri. Varkeychan T Vallamattam  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 0.798 Cr  
**Agreed Amount With GST** : Rs. 89,38,493.08  
**Site Handover date** : 08.03.2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

#### Status of Work in terms of components:

- Landscaping of cemetery area
- Lighting
- Conservation of ceiling
- Woodwork
- Joinery
- Electrical works

#### Status:

- Agreement Executed.
- Work yet to be started

## Lokanarkavu Temple

**Name of contractor** : Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 3.787 Cr  
**Agreed Amount With GST** : Rs. 4,24,19,523.2  
**Site Handover date** :  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 27-06-2022  
**Expected Date of completion** :

### Status of Work in terms of components:

- Museum of Folklore
- Oottupura
- Thanthrimadam - Museum of Myth
- Conservation of Small Chira, Kulappura
- Compound wall and step
- Conservation of Big Chira
- Electrical works
- Plumbing and toilet fittings for differentially abled
- Pavement works & Landscaping

### Status:

- Agreement Executed.
- Work yet to be started

## Makreri Subramanyaswami Temple

**Name of contractor** : Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 1.835 Cr  
**Agreed Amount With GST** : Rs. 2,05,52,642.3  
**Site Handover date** :  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 27-06-2022  
**Expected Date of completion** :

### Status of Work in terms of components:

- Oottupura
- Toilet Block
- Landscaping
- Electrical
- Streetscape ( Paving of Chuttambalam)
- Water supply and Sanitary Arrangements
- Stone Paving
- Conservation of pond
- Electrification

### Status:

- Agreement Executed.
- Work yet to be started
- MoU to be signed.

# **PROJECTS IN WAYANAD DISTRICT**

**KARAPUZHA PHASE  
III  
(TOURISM)**

**KARAPUZHA PHASE III  
CONSTRUCTION OF VIEWING  
TOWER, BAMBOO PAVILION  
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P  
Agreement date : 22/12/2017  
Agreed Amount : ₹ 7248330.00  
Agreed Amount With GST : Rs. 725000.00  
Site Handover date : 29/12/2017  
Project duration : 10 months  
Scheduled Date of Completion :29/10/2018  
Expected Date of completion :15/07/2021

**status of Work in terms of components:**

Viewing tower-97%  
Bamboo pavilion-100%  
Bridge.-100%

**Works done in the last week**

- Viewing tower-  
painting inside and  
outside

**Scheduled progress as on 31-07-2021 100%**

**Achieved progress as on 31-07-2021 - 97%**

**Last week progress in 0%**

**Current week progress - 20%**

**Current Bill Status :3rd bills submitted of amount 41,40,724.00**

**Current Financial Progress :60%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN KOZHIKODE DISTRICT



**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion :13-08-2021  
Expected Date of completion :13-09-2021

**Status of Work in terms of components:**

- Main Building Civil works – 76%
- Main Building Electrical works – 77%
- Main Building ELV Works - 63%

**Works done in the last week**

- Main Building Civil works
- Main Building Electrical works
- Main Building Plumbing works

**Scheduled progress as on 31-07-2021 - 96%**

**Achieved progress as on 31-07-2021 - 51%**


**Last week progress in 50%**

**Current week progress in 51%**

**Current Bill Status : CC 2<sup>nd</sup> and part submitted**

**Current Financial Progress : 25.8%**

**Images of works done at Site during last week (with time stamp)**

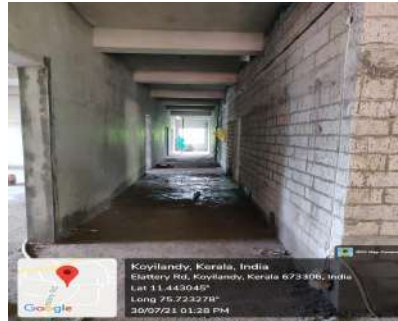

**PERUVANNAMOO  
ZHI (TOURISM)**

**DEVELOPMENT OF  
PERUVANNAMOOZHI DAM  
TOURISM PROJECT IN  
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N  
Agreement date : 06-11-2020  
Agreed Amount : ₹ 26359270.97  
Agreed Amount With GST : Rs. 31388620.00  
Site Handover date : 13/11?2020  
Project duration : 9 months  
Scheduled Date of Completion :12-08-2021  
Expected Date of completion :30-09-2021

**Status of Work in terms of components:**

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate

**Works done in the last week**

- Childrens park-fencing works
- Construction of new gate-pcc for plinth beam
- Walk way with handrails-filling quarry waste, handrail work in progress.
- Canteen-ceiling works.
- Interpretation

Scheduled progress as on 31-07-2021 - 60%

Achieved progress as on 31-07-2021 - 53%

Last week progress in 30%

Current week progress in 50 %

Current Bill Status : 1st bill-46,10,745.21

Current Financial Progress :20%

Images of works done at Site during last week (with time stamp)



**RCB  
PERINCHERIKADA  
VU  
(KIIFB)**

**CONSTRUCTION OF  
REGULATOR CUM BRIDGE AT  
U/S OF PERINCHERIKADAVU IN  
KUTTIADY RIVER  
(GULIKAPUZHA) AT  
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium  
Agreement date : 07-09-2020  
Agreed Amount : ₹ 6,11,33,413.18/-  
Agreed Amount With GST : ₹ 68,46,94,229/-  
Site Handover date : 17-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :16-03-2022  
Expected Date of completion :16-09-2022

**Status of Work in terms of components:**

- RCB – 2% (two piles casted)
- Bank Protection works – 1%
- Material collection works are going on.(Coconut posts supplying)

**Works done in the last week**

- The cross bund constructed was dismantled as per the instruction from Higher authorities of Irrigation department and local bodies. No works are possible in river without the bund.
- 

**Scheduled progress as on 31-07-2021 - 51%**

**Achieved progress as on 31-07-2021 - 2%**

**Last week progress in 2%**

**Current week progress 2%**

**Current Bill Status : NIL**

**Current Financial Progress : NIL**

**Images of works done at Site during last week (with time stamp)**



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

**KIIFB Project - Construction of  
Regulator at Puzhankavu across  
Kadalundi River**



Name of contractor : Infab Infrastructure Pvt Ltd  
Agreement date : 17-12-2019  
Agreed Amount : ₹ 9,79,65,435.62  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 17-12-2019  
Project duration : 18 months  
Scheduled Date of Completion :16/06/2021  
Expected Date of completion :15/02/2022

**Status of Work in terms of components:**

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

**Works done in the last week**

- Work is delayed due rainfall and rise in water level.

**Scheduled progress as on 30-07-2021- 100 %**

**Achieved progress as on 30-07-2021 - 55%**

**Last week progress in 55 %**

**Current week progress in 55 %**

**Current Bill Status : Total Bill submitted ₹3 Crores**

**Current Financial Progress in %: 8.67%**

**Images of works done at Site during last week**



**RCB  
Moothikkayam  
(KIIFB)**

**KIIFB Project construction of  
regulator cum bridge across  
thoothapuzha keezhmurikadavu  
moothikkayam in moorkanad  
panchayath**

Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022  
Expected Date of completion :26/12/2022

**Status of Work in terms of components:**

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

**Works done in the last week**

- No work has done due to monsoon.
- Consolidated survey nos for LA
- 

**Scheduled progress as on 01/08/2021 - 58 %**

**Achieved progress as on 01/08/2021 - 3%**

**Last week progress - 3%**

**Current week progress - 3%**

**Current Bill Status : First & part bill submitted – Rs 1.03 Cr**

**Current Financial Progress : 1.75%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMBUZHA  
(KASE)**

**UPGRADATION OF GOVT. ITI  
MALAMPUZHA ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS  
Agreement date : 05/03/20  
Agreed Amount : ₹11,61,93,745/-  
Agreed Amount With GST : Rs. 13,01,36,994.40/-  
Site Handover date : 16/03/2020  
Project duration : 18 months  
Scheduled Date of Completion : 05/09/2021  
Expected Date of completion : 29/06/22

**Status of Work in terms of components:**

- Main building part 2 roof slab completed
- Initial pile load test,routine test
- Smart classroom flooring and painting completed.
- Lower basement plinth beam work completed.
- FF part 1 area column rising completed.

**Works done in the last week**

- Pile cap casting 100%
- Lift area soil backfilling 95%
- Pile cap soil backfilling 100%
- UGF block work under progress
- LGF retaining wall steel work under progress
- LGF roof slab concreted.
- UGF plinth beam 95% completed.

Scheduled progress as on 30/07/2021- 92%

Achieved progress as on 30/07/2021 - 33%

Last week progress - 1%

Current week progress - 1%

Current Bill Status : no of bill submitted - 1, amount:- 68,83,336

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Scheduled progress as on 31/07/2021 - 38 %**

**Achieved progress as on 24/07/2021 - 27 %**

**Last week progress - 1%**

**Current week progress - 1%**

**Current Bill Status : 1 st bill submitted of 1.56 cr**

**Current Financial Progress : 0%**

**Images of works done at Site during last week**

**Status of Work in terms of components:**

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(35m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 2 pier and 2nd Lift of 3 pier is completed

**Works done in the last week**

- No major civil works due to high flood





**Moongilmada LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of contractor** : M/s poljo Vyapar kendra Pvt Ltd  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹33288750 Crores  
**Agreed Amount With GST** : Rs. 37283400/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :26-02-2022  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

- Work Stopped due to Rain

**Scheduled progress as on 30/07/2021 - 42 %**

**Achieved progress as on 30/07/2021 - 40.5 %**

**Last week progress in : 40.5%**

**Current week progress : 0%**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**

**Karadippara LIS  
(WRD-RKI )**

**KIIDC-Providing Community  
micro irrigation at karadipara LIS  
in eruthenpathy Panchayath  
palakkad district**

**Name of contractor** :M/s poljo Vyapar kendra Pvt Ltd  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹2,34,53,555.40 Crores  
**Agreed Amount With GST** : Rs. 26267982.04/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :26-02-2022  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

- Work Stopped due to Rain

**Scheduled progress as on 30/07/2021 - 44 %**

**Achieved progress as on 30/07/2021 - 84 %**

**Last week progress in : 84 %**

**Current week progress in 0%**

**Current Bill Status : NO**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**

**Karadipara  
(Civil)**

**KIIDC-Providing Community  
micro irrigation at karadipara LIS  
in eruthenpathy Panchayath  
palakkad district-Civil**

Name of contractor :M/s Vallamattam constructions  
Agreement date : 26-02-2021  
Agreed Amount : ₹16,41,529.18 Lakhs  
Agreed Amount With GST : Rs. 18,38,512.68/-  
Site Handover date : 26-02-2021  
Project duration : 6 months  
Scheduled Date of Completion :26-08-2022  
Expected Date of completion :31-08-2021

**Status of Work in terms of components:**

- Construction of Pump House
- Electrification

**Works done in the last week**

- Plastering work
- PCC for floor

**Scheduled progress as on 30/07/2021 - 34 %**

**Achieved progress as on 30/07/2021 - 65 %**

**Last week progress in : 52%**

**Current week progress in 13%**

**Current Bill Status : No**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN THRISSUR DISTRICT

**ITI CHALAKUDY**

**UP GRADATION OF GOVT ITI  
CHALAKUDY ON PAR WITH  
INTERNATIONAL STANDARDS**



Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

Scheduled progress as on 30-07-2021 - 0 %

Achieved progress as on 30-07-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)


### Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### Works done in the

#### last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

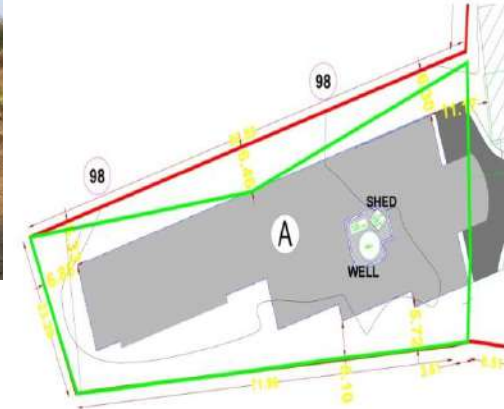

# PROJECTS IN ERNAKULAM DISTRICT

**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

Name of contractor : Marymatha construction  
Agreement date : 04-01-2021  
Agreed Amount : ₹24.36 Cr  
Agreed Amount With GST : Rs. 272,843,729.92  
Site Handover date : 14-01-2021  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2022  
Expected Date of completion :

**Status of Work in terms of components:**

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

**Works done in the last week**

- NO WORK

Scheduled progress as on 30-07-2021 - 21 %

Achieved progress as on 30-07-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

**IMPROVEMENTS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY**

Name of contractor : Southern Tech  
Agreement date : 08-10-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 04-12-2019  
Project duration :15 months  
Scheduled Date of Completion :07-01-2020  
Expected Date of completion :30-08-2021

**Status of Work in terms of components:**

- Cleaning & desilting- completed
- Side protection work- 81%
- Road and walkway formation- 58%
- Fencing and Handrail work-55%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%(tile work remaining)

**Works done in the last week**

- Fixing GI post ch320-900 (RB)
- Epoxy painting - fencing post ch320-690 (RB & LB)
- Welding & placing the fencing frame Ch 0-900(RB & LB)
- Top Belt concreting

**Scheduled progress as on 30-07-2021 - 98%**

**Achieved progress as on 30-07-2021 - 93.25%**

**Last week progress - 93%**

**Current week progress -93.25%**

**Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00**

**Current Financial Progress : 65%**

**Images of works done at Site during last week (with time stamp)**



**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY—PROVIDING  
STREET LIGHTS ALONG THE  
PATHWAYS OF  
ANTHAKARATHODE**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 08-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 31-07-2021

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-50%
- Placing of lamp post, LED & feeder -30%
- Excavation and concreting-65%

**Works done in the last week**

- No work

**Scheduled progress as on 30-07-2021- 85%**

**Achieved progress as on 30-07-2021- 44%**

**Last week progress - 43%**

**Current week progress 44%**

**Current Bill Status : First and Part Bill prepared**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**





# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

**UP GRADATION OF GOVT ITI  
KATTAPPANA ON PAR WITH  
INTERNATIONAL  
STANDARDS**

Name of contractor : Anchanical constructions  
Agreement date : 16.10.2020  
Agreed Amount : Rs 4,76,87,560.83  
Agreed Amount With GST : Rs 5,34,10,068.1  
Site Handover date : 04-12-2019  
Project duration : 08 months  
Scheduled Date of Completion : 24-02-2022  
Expected Date of completion : 24-02-2022

**Status of Work in terms of components:**

- Work slowed down due to rain.
- Reinforcement works of grade beam - 15 %
- Grade beam concrete- 3%

**Works done in the last week**

- . Grade beam reinforcement work.
- Grade beam concrete

**Scheduled progress as on 31-07-2021 - 22%**

**Achieved progress as on 31-07-2021 - 19.5%**

**Last week progress : 19.5%**

**Current week progress :19.9%**

**Current Bill Status : NIL**

**Current Financial Progress in %:NIL**

**Images of works done at Site during last week**



**PAVANATHA  
COLLAGE  
MURIKKASSERY  
(RUSA )**

**RUSA II PROJECT -  
CONSTRUCTION-PAVANATHMA  
COLLEGE MURIKKASSERI,  
IDUKKI.**

**Name of contractor** : Anchanical constructions  
**Agreement date** : 02.12.2019  
**Agreed Amount** : Rs.79,00,000  
**Agreed Amount With GST** : Rs.93,22,000  
**Site Handover date** : 02-06-2020  
**Project duration** : 09 months  
**Scheduled Date of Completion** :31-08-2021  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

**Works done in the last week**

- No works done.

**Scheduled progress as on 31-07-2021 - 94%**

**Achieved progress as on 31-07-2021 - 89%**

**Last week progress : 89%**

**Current week progress in : 89%**

**Current Bill Status : 2 Bills submitted, RS 54,77,389.30**

**Current Financial Progress : 69%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – I  
(TOURISM)**

**ADDITIONAL WORK I OF ECO  
LODGE CONSTRUCTION AT  
IDUKKI (CONSTRUCTION OF  
APPROACH ROAD,RETAINING  
WALL,DRAIN AND STREET  
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.  
Agreement date : 11-08-2020  
Agreed Amount : Rs.69,50,003.24  
Agreed Amount With GST : Rs. 77,84,003.36  
Site Handover date : 21-08-2020  
Project duration : 04 months  
Scheduled Date of Completion : 31-08-2021  
Expected Date of completion : 08-07-2021

**Status of Work in terms of components:**

- Interlocking pathway 95%
- Gate installation 70%
- Providing street lights - 60%

**Works done in the last week**

- Pathway interlocking
- Rain delayed work progress.

**Scheduled progress as on 31-07-2021 - 91%**

**Achieved progress as on 31-07-2021 - 95%**

**Last week progress : 95%**

**Current week progress : 98%**

**Current Bill Status : 1 Bill submitted, RS 36,27,077.98.**

**Current Financial Progress : 52%**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

**UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI**



Name of contractor :SRI BIBY SCARIA  
Agreement date : 30-06-2020  
Agreed Amount : Rs.1,45,51,908.00  
Agreed Amount With GST : Rs. 1,71,71,251.44  
Site Handover date : 13-07-2020  
Project duration : 9 months  
Scheduled Date of Completion :13-04-2021  
Expected Date of completion : 13-09-2021

**Scheduled progress as on 31-07-2021 - 70 %**

**Achieved progress as on 31-07-2021 - 27 %**

**Last week progress in % -26.4%**

**Current week progress - 27%**

**Current Bill Status : prepared**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Roofing works of guest house building is completed
- 95% of roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building completed.

**Works done in the last week**

- Roofing works of guest house building



PANCHALIMEDU  
(TOURISM)

PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAMVILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM  
Agreement date : 22/12/2020  
Agreed Amount : ₹2,43,99,440.78  
Agreed Amount With GST : Rs. 2,73,27,373.67  
Site Handover date : 01-01-2021  
Project duration : 12 months  
Scheduled Date of Completion : 31-12-2021  
Expected Date of completion : 31-12-2021

**Scheduled progress as on 31-07-2021 - 35 %**

**Achieved progress as on 31-07-2021 - 17 %**

**Last week progress - 17 %**

**Current week progress - 17 %**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

**Works done in the last week**

- Work stopped due to heavy rain and mist.
- Meeting and site visit is conducted to discuss about the construction of check dam.
- Attendance
  - 1) sri K T Binu ( district panchayath member )
  - 2) smt.Baby sheeja ( DD, tourism dpt.)
  - 3)sri Gireesh ( secretary DTPC Idukki)
  - 4) Er. Haran Babu sir( DGM, KIIDC)
  - 5) Er. Sarath sir (PCO, KIIDC)
  - 6)sri Abhiram ( Project coordinator, DTPC)
  - 7) sri Atheesh P Mohan (CPE, KIIDC)
  - 8) sri Dileep (contractor )
  - 9) sri Rajesh (site engineer-contractor)



# PROJECTS IN KOTTAYAM DISTRICT

**ITI  
ETTUMANOOR  
(KASE)**

**UP GRADATION OF GOVT ITI  
ETTUMANOOR ON PAR WITH  
INTERNATIONAL STANDARDS**

**Name of contractor** : Swathy Construction  
**Agreement date** : 30-07-2020  
**Agreed Amount** : ₹ 6,95,25,557.81  
**Agreed Amount With GST** : ₹ 7,78,68,624.74  
**Site Handover date** : 10-08-2020  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 09-08-2021  
**Expected Date of Completion** : Within this Financial Year

**Scheduled progress as on 31/07/2021- 98 %**

**Achieved progress as on 31/07/2021 - 44 %**

**Last week progress - 44%**

**Current week progress - 1%**

**Current Bill Status : CC 3<sup>rd</sup> and part is submitted (total : ₹ 2,24,79,461.06)**

**Current Financial Progress : 32%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main building civil works (70%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting (0%)
- Fire protection works (0%)
- Furniture for existing smart class room  
Converted to smart class rooms (0%)

**Works done in the last week - Main building civil works**

- AAC block work on FF
- Lintel and sunshade shuttering and reinforcement, it's concrete works on UGF.
- Electrical concealed works
- Fin wall at front UGF
- Plastering



**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE  
INSTITUTE OF HOTEL  
MANAGEMENT STUDIES AT  
PALA, KOTTAYAM DISTRICT,  
CONSTRUCTION OF ACADEMIC  
BLOCK**

**Name of contractor** : SITCO Associates  
**Agreement date** : 01-03-2016  
**Agreed Amount** : ₹13.48 Cr  
**Site Handover date** : 10-03-2016  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 31/10/2017  
**Expected Date of completion** : 31/12/2021

**Scheduled progress as on 31/07/2021 - 90%**

**Achieved progress as on 31/07/2021 - 80%**

**Last week progress -79%**

**Current week progress - 1%**

**Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18**

**Current Financial Progress : 74 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works done in the last week**

- Water tank cover slab shuttering and reinforcement works



**CHEEPUNKAL  
(TOURISM)**

**KI IDC KUMARAKOM  
CHEEPUNKAL DESTINATION  
DEVELOPMENT PROJECT AT  
AYMANAM PANCHAYAT IN  
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1,19,66,517.41  
Agreed Amount With GST : ₹ 1,34,02,499.49  
Site Handover date : 05-05-2021  
Project duration : 12 months  
Scheduled Date of Completion : 04-05-2022  
Expected Date of Completion : 04-05-2022

**Status of Work in terms of components:**

- House Boat Jetty (0%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

**Works done in the last week - Main building civil works**

- Reinforcement work for Pile
- Casting of Precast concrete piles

**Scheduled progress as on 31/07/2021-**

**Achieved progress as on 31/07/2021 - Nil**

**Last week progress -**

**Current week progress -**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN ALAPPUZHA DISTRICT

**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR  
WITH INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction  
Agreement date : 15/10/2020  
Agreed Amount : Rs 18 Cr  
Agreed Amount With GST : Rs20,64,45672/-  
Site Handover date :23/10/2020  
Project duration :18 months  
Scheduled Date of Completion : 22/04/2022  
Expected Date of completion :22/3/2022

Scheduled progress as on 31/07/2021 -42%

Achieved progress as on 31/07/2021 -Nil

Last week progress in - Nil

Current week progress in - Nil

Current Bill Status : (no: of bills submitted with amount) Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)- Nil

#### **Status of Work in terms of components:**

- Main building civil works (0%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room

#### **Works done in the last week**

- Tree cutting has been taken for open tender, and the amount accepted has given to directorate for approval.The accepted amount has been given to government for approval.
- Meeting was arranged on 15/7/2021 by KASE,KIIDC AND CHENGANNUR ITI Principal and discussed the various issue regarding the treecutting and KIIFB query and sorted out conclusion

**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

**MODERNIZING WATER  
TRANSPORT IN ALAPPUZHA  
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-09-2021

**Status of Work in terms of components:**

- Cleaning of Canals Completed
- Deepening of Canals after dewatering Completed
- RR Masonry side protection
  - Main Canals Completed
  - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
  - Culvert Structural Works Completed
  - Approach wall Under progress

**Works done in the last week**

- Bund removal for Bernad, Devi wire culverts
- Rubble works for bernad culvert.
- Earth backfilling for Ambanakulangara culvert

**Scheduled progress as on 30/07/2021 - 100%**

**Achieved progress as on 30/07/2021 - 92.25%**

**Last week progress in 92.00%**

**Current week progress- 0.25%**

**Current Bill Status : Rs.38,13,65,683.22 upto 4th bill**

**Current Financial Progress : 70%**

**Images of works done at Site during last week (with time stamp)**



**PUNNAMADA  
(TOURISM WORK )**

**Punnamada- Starting Point  
Pathway and Boat Landing at  
Alapuzha District.**



Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.11 Cr  
Agreed Amount With GST : Rs. 1,23,77,355.31  
Site Handover date : 05-05-2021  
Project duration : 6 months  
Scheduled Date of Completion : 04-11-2021  
Expected Date of completion : 04-11-2021

**Status of Work in terms of components:**

- Pathway  
Solar Lighting

**Works done in the last week**

- The mobilization works for carrying out the components under progress

**Scheduled progress as on 30/07/2021- 20%**

**Achieved progress as on 30/07/2021 - 0%**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**

**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL  
)- KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 04-02-2022

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- The mobilization works for carrying out the components under progress

**Scheduled progress as on 30/07/2021 - 15%**

**Achieved progress as on 30/07/2021 - 0%**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**

**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 51.3 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Status of Work in terms of components:**

- 20m groynes – (5 nos) - Not Started
- 30M GROYNES - 7nos- 2 completed
- 40M GROYNES – 9 nos - 1 in progress
- 50M GROYNES – 9 nos - 3 in progress
- Sea wall length - 305 m – Not started
- 30514 MT boulders reached out of 178922 MT (17 %)
- 2T TETRAPODS – 6843 nos. casted out of 23902 nos.
- 5T TETRAPODS – 547 nos. casted out of 2956 nos.
- Earthwork Excavation – 9359.27m3 completed out of 45955.7 M3

**Works done in the last week**

- 2T tetrapod casted - 379 nos.
- 5T tetrapod casted -17 nos.
- Supplying and Laying of Boulders - 6097.7 MT
- laying of boulders for G5, G6, G7 and G8 are in progress.
- Groyne work started for G9
- Earthwork Excavation and geomat laying was done for G9 and G22

**Scheduled progress as on 31-07-2021 – 60 %**

**progress as on 31-07-2021 - 28 %**

**Last week progress - 2 %**

**Current week progress - 3 %**

**Current Bill Status** : 2 bill submitted for an Amount of Rs. 11,23,21,298

**Current Financial Progress : 13.62 %**

**Images of works done at Site during last week (with time stamp)**



**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**

**Name of contractor** : Ramalingam construction Company Pvt. Ltd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹26. 23Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :29-01-2022  
**Expected Date of completion** :29-05-2022

**Status of Work in terms of components:**

- 1.20M GROYNES - 6 NOS-Not started
- 2. 25M GROYNES - 15 NOS-Not started
- 3. SEA WALL LENGTH - 40m  
-Not started
- 4. TOTAL QUANTITY OF BOULDERS - 94497 MT
- 7. 2T TETRAPODS -940 nos casted out of 9874 NOS
- 8. 5T TETRAPODS - 2385 NOS
- 9. GEOMAT - 64739 M2
- 10. EARTHWORK EXCAVATION - 3290 M3

**Works done in the last week**

-Tetrapod casting is started and Total no of cased tetrapod s,2T-297nos

**Scheduled progress as on 31/07/2021 - 60%**

**Achieved progress as on 31/07/2021 - 2.5%**

**Last week progress -2%**

**Current week progress -2%**

**Current Bill Status :1 part bill susubmitted for an amount of Rs 1715000.00**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**



**Name of contractor** : Ramalingam construction Company Pvt. Lmtd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹20.08Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2 NOS-One is started and in progress
2. 30MGROYNES -4 NOS-2 nos are started and in progress
3. 50M GROYNES - 7 NOS- 1 is started
4. 7684MT boulders reached out of 74546 MT
5. 2T TETRAPODS -3754casted out of 8930NOS
6. 5T TETRAPODS -214 nos casted out of 1199NOS
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154 M3

**Works done in the last week**

- 2T and 5T tetrapod casting is in progress
- The total no.of tetrapods casted 2T-215 and 5T-33nos
- Geomat layed for G3&G4
- Supplying and laying of boulders-2767.7MT

**Scheduled progress as on 31/07/2021 - 60%**

**Achieved progress as on 31/07/2021 -15%**

**Last week progress in - 3.5%**

**Current week progress in 3%**

**Current Bill Status** : 2 part bills submitted for an amt of Rs 23596744.04

**Current Financial Progress in %:** Nil

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2NOS-Not started
2. 30M GROYNES -10 NOS-Not started
3. 40M GROYNES - 4 NOS- Not started
4. TOTAL QUANTITY OF BOULDERS - 101487 MT
5. 2T TETRAPODS - 2921nos casted out of 8941 NOS
6. 5T TETRAPODS - 3432 NOS
7. GEOMAT - 76299M2
8. EARTHWORK EXCAVATION – 6239M3

**Works done in the last week**

-The total no.of tetrapods casted  
2T -174nos and  
5T is 0

**Scheduled progress as on 31/07/2021 - 60 %**

**Achieved progress as on 31/07/2021 - 7 %**

**Last week progress - 2%**

**Current week progress - 2%**

**Current Status : 2 part bills submitted for an amt of Rs15862000.00**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**



**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne at Kattoor**  
from Ch.168.465KM TO CH 171.627KM (Old CH 96.643KM TO CH  
9.535 KM)

**Name of contractor** : Ramalingam Construction  
Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 49.04 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Scheduled progress as on 31-07-2021 – 66 %**

**Achieved progress as on 31-07-2021 - 21.60 %**

**Last week progress - 1.80%**

**Current week progress - 4 %**

**Current Bill Status** : 2 bill submitted for an Amount of Rs. 7,01,81,077.49

**Current Financial Progress : 9.12 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 20m groyne - 3 nos – Not started
- 30m Groyne -7 nos – not started
- 40m groyne - 24 nos- not started
- Laying of boulders - Not started
- 2T TETRAPODS – 7749 nos.  
casted out of 21562 nos.
- 5T TETRAPODS – 405 nos. casted  
out of 3144 nos.
- Geomat - 112083 m2
- Earthwork Excavation - 42122 M3

**Works done in the last week**

- 2T tetrapod casted - 417 nos.
- 5T tetrapod casted - 35 nos.
- Supplying and Laying of Boulders - 4700 MT
- laying of boulders for G13, G14, G15 are in progress.
- Groyne work started for G16 and G26
- Earth work and mat laying also done for Groyne



# PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**

Name of contractor : Asian Constructions  
Agreement date : 16-12-2020  
Agreed Amount : ₹3.65 Cr  
Agreed Amount With GST : Rs. 4,09,28,822.77  
Site Handover date : 24-12-2020  
Project duration : 8 months  
Scheduled Date of Completion :23-08-2021  
Expected Date of completion :31-12-2021

Scheduled progress as on 30/07/2021 - 75 %

Achieved progress as on 30/07/2021 - 13%

Last week progress -13%

Current week progress -14%

Current Bill Status : (no: of bills submitted with amount) - NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Main building civil works –20%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 18%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

**Works done in the last week**

- Main building civil works - Backfilling and compaction completed





**Thenmala  
(Tourism Project)**

**IMPROVEMENT AND  
DEVELOPING ECO-TOURISM AT  
THENMALA DAM IN KOLLAM  
DISTRICT**

Name of contractor : Tomy Vallamattom  
Construction  
Agreement date : 29-10-2020  
Agreed Amount : ₹4.5 Cr  
Agreed Amount With GST : Rs. 4,49,90,000.00  
Site Handover date : 09-11-2020  
Project duration : 15 months  
Scheduled Date of Completion : 08-02-2022  
Expected Date of completion : 07-01-2022

Scheduled progress as on 31/07/2021 - 48%

Achieved progress as on 31/07/2021 - 10%

Last week progress in -10%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- SHOP (7.1%)
- Shed to shop (40%)
- Building Renovation (35%)
- Children play (1%)
- Water tank (15%)
- Security cabin (2%)
- Toilet and cloak room (2%)

**Works done in the last week**

- Shop- lintel completed in two span.
- Reinforcement work for water tank started
- Water tank column for 1m concreted completed
- Water tank column plinth beam completed
- Filling excavation completed
- Clearing site for toilet and



**ITI  
DHANUVECHAPU  
RAM  
(KASE)**

**UPGRADATION OF GOVT. ITI  
DHANUVECHAPURAM ON PAR  
WITH INTERNATIONAL  
STANDARDS**

Name of contractor : Heather Construction  
Agreement date : 25-11-2019  
Agreed Amount : ₹11.18 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 04-12-2019  
Project duration : 20 months  
Scheduled Date of Completion : 03-08-2021  
Expected Date of completion : 03-08-2021

Scheduled progress as on 30-07-2021- 80%

Achieved progress as on 30-07-2021 - 73%

Last week progress - 68%

Current week progress - 73%

Current Bill Status :6 bill were passed, Amount up to 8th bill:55712783.40/-  
,8<sup>th</sup> bill submitted amount:3784498.15/-

Current Financial Progress :49%

### Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 90% completed
- GF primer work 80% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 30% completed
- FF Block Work 92% completed
- FF Ceiling work 70% completed
- FF plastering 85% completed
- Dummy column RCC completed
- FF Electrical concealed work 65% completed
- Parapet plastering 90% completed
- GF Tile work 52%
- FF primer work 60% completed

### Works done in the

#### last week

- Outside Plastering
- car porch footing concrete
- GF-Toilet Wall Tiling work

